

Work Order ID 133751

Tuesday, June 16, 2015 2:55:10 PM

133751

Page 1

Item ID: D4306-044 Accept *N900040100* Setup Start *NS1*
 Revision ID: Stop *NS2*
 Item Name: Rib Assembly, RH
 Start Date: 6/16/2015 Start Qty: 3.00 *3* Cust Item ID:
 Required Date: 6/16/2015 Req'd Qty: 3.00 *3* Customer:
 Reference:

Approvals: Process Plan: MCS Date: JUN 16 2015 Tooling: _____ Date: _____ Run Start *NR1*
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop *NR2*

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
Draw Nbr	Revision Nbr								
D4306	C								

100 Weld per dwg A/R S.S. rod Batch 413417 0.00 15.00.22 3 DAS 43 JAN 27 2016
 100
 Large Fab
 Large Fab

Memo
 1- Cut tube 52"
 2- Bend tube with manuel pipe bender as per DT9920
 *** Make line at 10.00" and use jig for other lines, and ensure seam in place on side of tube when bending***
 3- Trim access tube material to finish size and cut notch as per dwg D4306-4 using DT9920 template
 4- Drill and chamfer holes as per dwg D4306-4 using DT9710
 5- weld bushing as per dwg D4306
 6- grind welds flush

110 QC6- Inspect dimensions to drawing 0.00 3 DAS 24 JAN 27 2016
 110
 QC
 Quality Control

Memo 0.00

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐								
Misidentified ☐	Past Due ☐	OTHER : _____							

Work Order ID 133751

133751

Page 2

Tuesday, June 16, 2015 2:55:10 PM

Item ID: D4306-044 Accept *N900040100* Setup Start *NS1*
 Revision ID: Stop *NS2*
 Item Name: Rib Assembly, RH
 Start Date: 6/16/2015 Start Qty: 3.00 *3* Cust Item ID:
 Required Date: 6/16/2015 Req'd Qty: 3.00 *3* Customer:
 Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start *NR1*
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop *NR2*

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
120	QC9- Inspect visual per QSI004- Fusion Welds	0.00							
120						3		DAS 24 9-89	JAN 27 2016
QC	Memo	0.00							
Quality Control									
130	Identify as per dwg & Stock Location: <i>WIP</i>	0.00							
130						3		DAS 43 9-89	JAN 27 2016
Packaging	Memo	0.00							
Packaging	LOCATION: WA004								
140	QC21- Final Inspection - Work Order Release	0.00							
140									
QC	Memo	0.00							
Quality Control									

ML5 JAN 27 2016

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
							Completed By		
							Lead hand / Supervisor Approval Verification		
							QC / QA Coordinator Approval		

Root Cause				FAULT CATEGORY			
Environment ☐	☐	No Re-verification	☐	Pressure/Forced	☐	Temperature/Cure	☐
Design ☐	☐	Operator	☐	Bending	☐	Set-up	☐
Doc/Data ☐	☐	Offset/Setup	☐	Centre Not Concentric	☐	BOM/Route	☐
Equip/Tooling ☐	☐	Supplier	☐	Cracks	☐	Broken/Damage/Defect	☐
Handling/Pre ☐	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐	Inspection Incomplete/Unqualified	☐
Material ☐	☐	Use for Testing	☐	Cuffs	☐	Contamination	☐
Internal Transport ☐	☐	Poor Information	☐	Crushing	☐	Countersink	☐
Tribal Knowledge ☐	☐	Rushing	☐	Heat Treat	☐	Cut Too Short	☐
LOA ☐	☐	Product Improvement	☐	Wave/Twist in Tube	☐	Instructions Incomplete/Unclear	☐
Substation ☐	☐	Process Improvement	☐	Marks/Chatter	☐	Drill Holes	☐
Past Expiry Date ☐	☐	Manufacturing Process	☐	OTHER : _____			
Misidentified ☐	☐	Past Due	☐				

Picklist Print

Tuesday, June 16, 2015 2:55:13 PM

Page 1

Work Order ID: 133751

133751

Parent Item: D4306-044

D4306-044

Parent Item Name: Rib Assembly, RH

Start Date: 6/16/2015

Required Date: 6/16/2015

Start Qty: 3.00

Required Qty: 3.00

Comments: IPP Rev:A 11.01.20 new issue DD verf:EC
11.03.03 AS PER DWG REV.C DD verf:EC

IPP Rev:B

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
---------------------------------	------------------------	---------------	-------------	---------------------	------------------	-----------------	--------------------	----------------	-------------	--------------	---------------	----------------	--------

D3759-1

Manufactured No

100

Each

177.0000

4

12

DAS
43
9-89

D3759-1

****B138897 → 12**

JAN 26 2016

Bushing

Location

Loc Qty

Loc Code

WA004

177

116816

59

117449

2

130893

18

132468

90

132855

8

M304TS0.750W.049

Purchased

No

100

f

668.5750

4.166

14

M304TS0 750W 049

304 SQ Tube .75x.75x.049W

Location

Loc Qty

Loc Code

WA004

668.575

M130871

84.4

M131128

13.175

M131868

571

Dh 15/6/22
11/32744 → 14 feet

DQA: _____ Date: _____




WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____


Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition			
10				Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabelled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : ☐					


ITEM	QTY -043	QTY -044	QTY -045	P/N	DESCRIPTION
	X			D4306-043	RIB ASSY, LH
		X		D4306-044	RIB ASSY, RH
			X	D4306-045	RIB ASSY
1	4	4	4	D3759-1	BUSHING
2	1			D4306-3	RIB
3		1		D4306-4	RIB
4			1	D4306-5	RIB

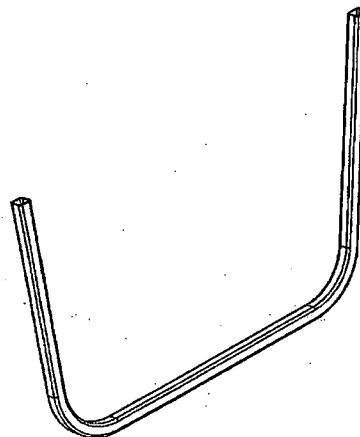


D4306-1 RIB

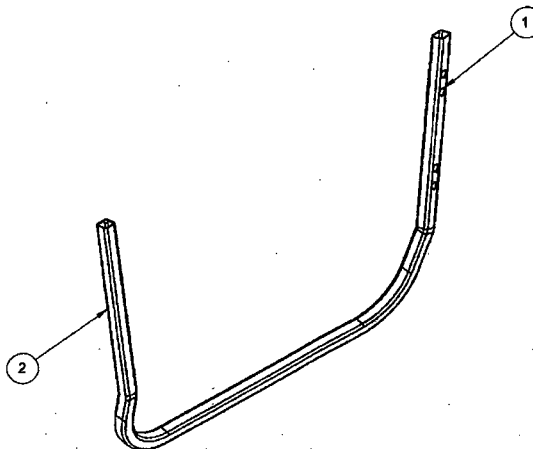

D4306-043 RIB ASSY, LH

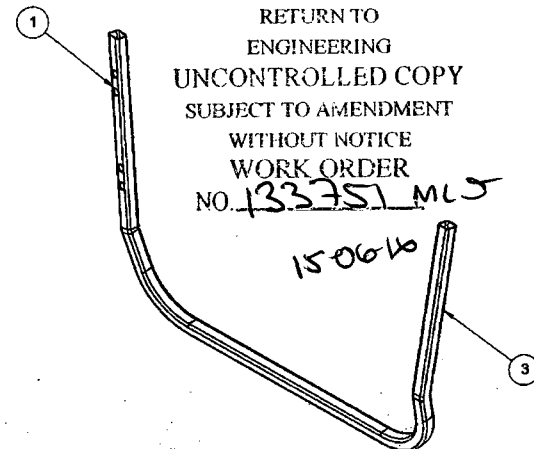

D4306-044 RIB ASSY, RH

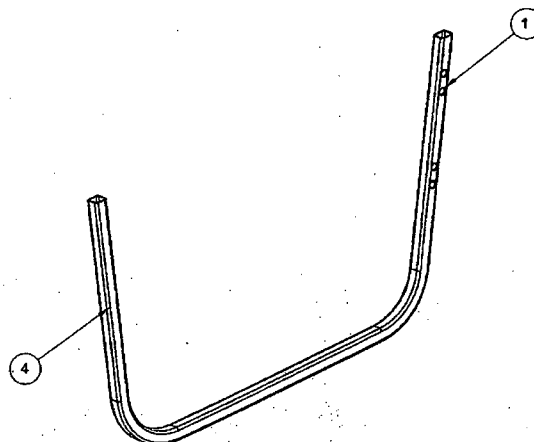



D4306-045 RIB ASSY

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 133751 MLJ
150616

RELEASED
2011-03-19

C	REFERENCE LENGTH CHANGED TO 52.0" FOR D4306-3, D4306-4 RIBS (A7-4/-6); INCREASED LENGTH OF D4306-3, D4306-4 RIBS BY 0.65" (C7-4, C8-4, C1-6, C2-6); CHANGED CUT ANGLE FROM 19° TO 22° (B8-4, B1-6); ADDED 4.50" REF DIM ON D4306-043/D44 (B6-3, B3-5)		SC	11.02.09
B	D4306-043, D4306-044, D4306-045 ADDED		SC	10.12.17
A	NEW ISSUE		CP	10.11.29
REV.		DESCRIPTION	BY	DATE
DESIGN	CP	DART AEROSPACE LTD HAWKESSBURY, ONTARIO, CANADA DRAWING NO. D4306 TITLE RIB SCALE NTS SHEET 1 OF 8 REV. C DATE 11.02.09		
DRAWN	SC			
CHECKED	SC			
MFG. APPR.	SC			
APPROVED	SC			
DE APPR.	SC			
DATE		COPYRIGHT © 2019 BY DART AEROSPACE LTD THIS DOCUMENT IS UNCLASSIFIED AND IS RELEASED ON THE CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR TO BE REPRODUCED OR TRANSMITTED IN ANY FORM OR BY ANY MEANS WITHOUT PERMISSION FROM DART AEROSPACE LTD.		

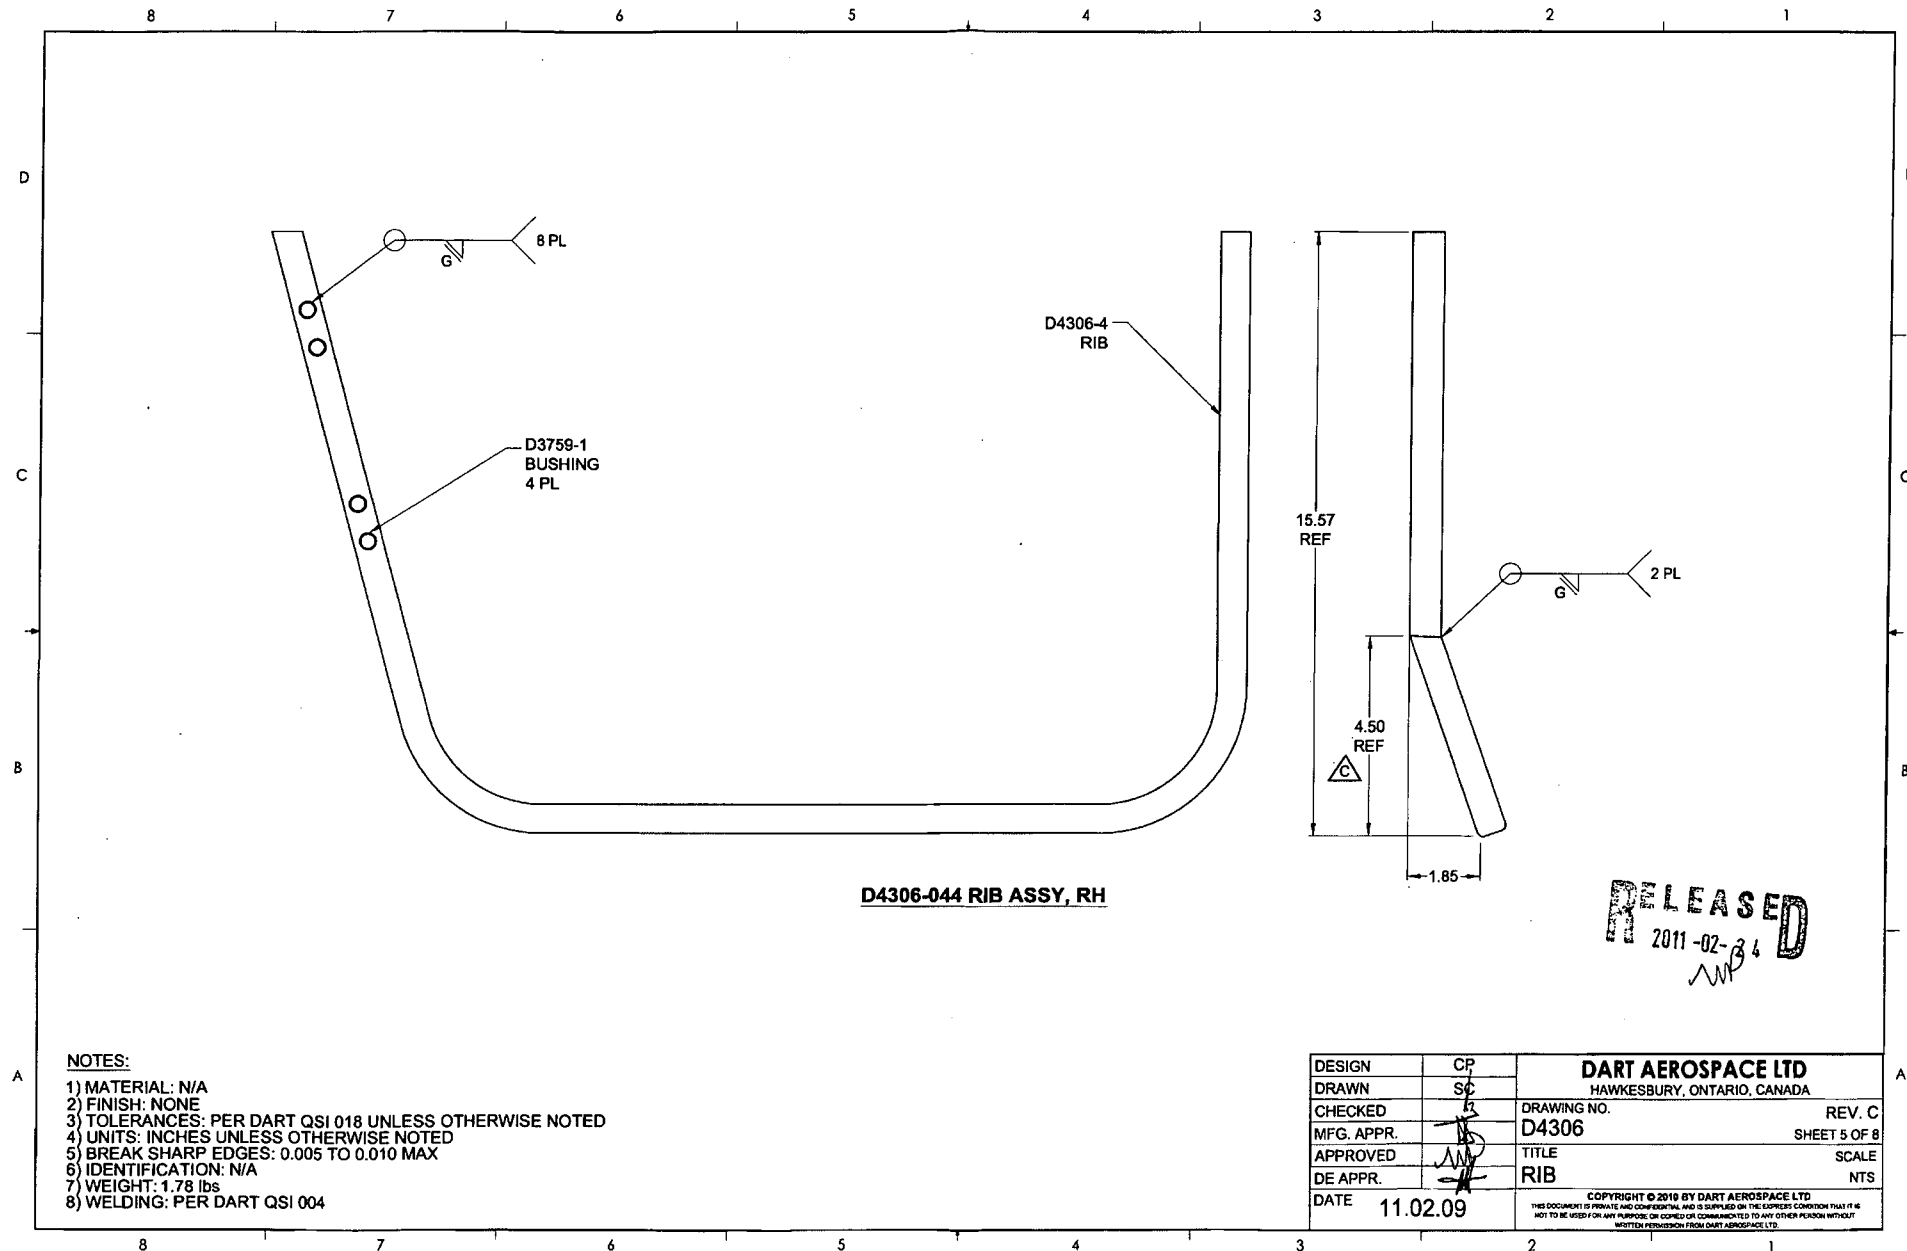

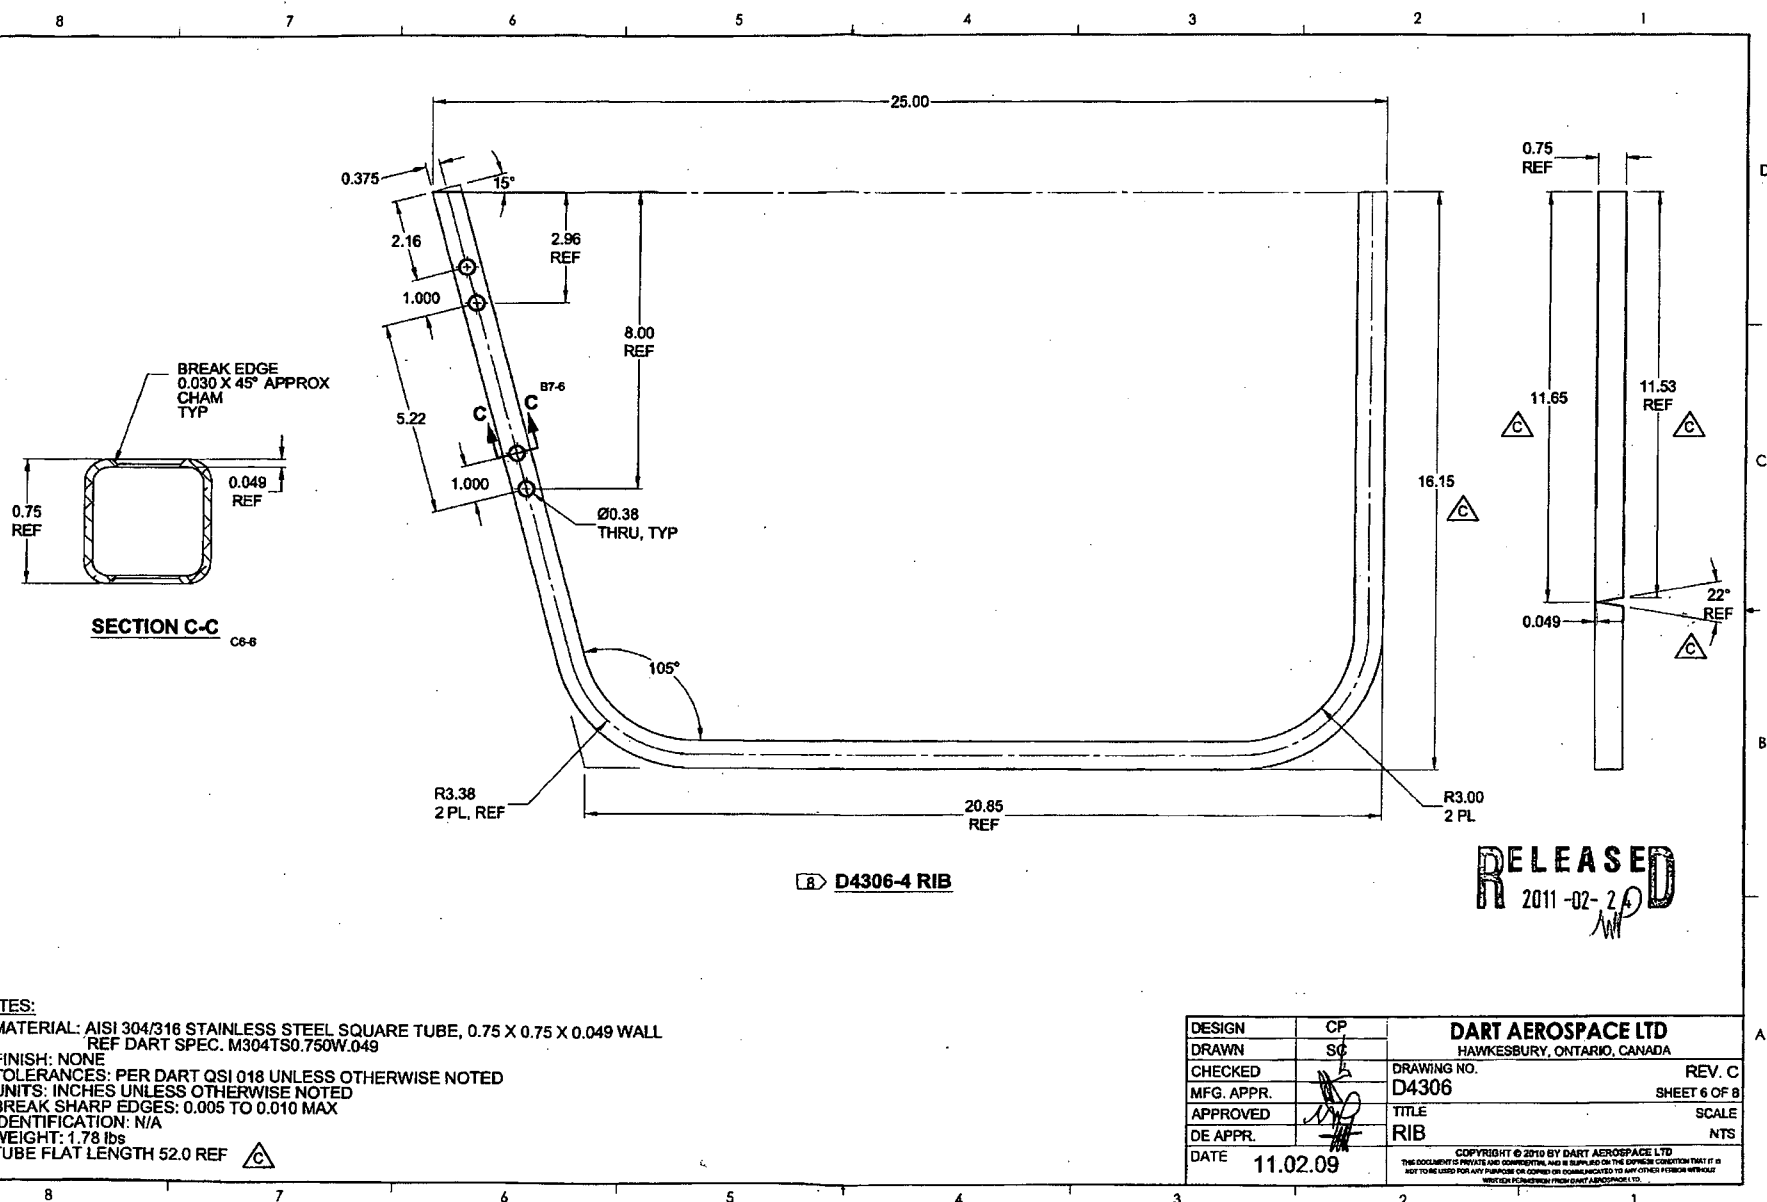

NOTES:

- 1) MATERIAL: AISI 304/316 STAINLESS STEEL SQUARE TUBE, 0.75 X 0.75 X 0.049 WALL
REF DART SPEC. M304TS0.750W.049
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: N/A
- 7) WEIGHT: 1.78 lbs
- 8) TUBE FLAT LENGTH 52.0 REF

DESIGN	CP	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	SC		
CHECKED	SC	DRAWING NO. D4306	REV. C
MFG. APPR.			SHEET 6 OF 8
APPROVED		TITLE RIB	SCALE
DE APPR.			NTS
DATE	11.02.09	COPYRIGHT © 2010 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COMPILED OR REPRODUCED IN ANY MANNER WITHOUT THE WRITTEN PERMISSION FROM DART AEROSPACE LTD.	
